
LINCOLN ROAD




OCEAN DRIVE

SOUTH BEACH PROMENADE
UPDATE

Completed Tasks

- Concepts coordinated with City departments and approved by FERC
- Tactical urbanism scope analyzed and reduced to defer Drexel Avenue component until a feasible strategy to mitigate parking impacts is identified
- Received direction from FERC to use the allocated $200K budget on Tactical Urbanism improvements for:
  - Española Way West from Pennsylvania to Drexel avenues
  - Española Way East from Washington to Collins avenues
  - 14th Court alleyway from Collins Avenue to Ocean Drive
- New traffic data collected to reflect current Washington Ave configuration
- Revised traffic study submitted to County for review

PROJECT FOCUS

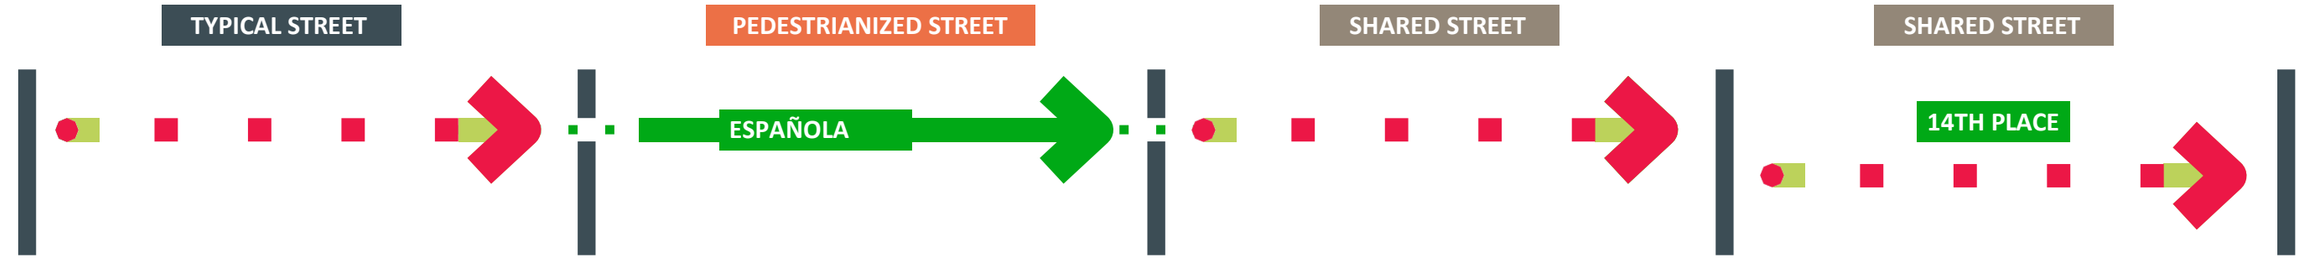

PENNSYLVANIA



Pennsylvania to

Stamped asphalt to match general paving pattern of pedestrianized segment of Española Way


DREXEL AVE



Drexel to Washington

Constructed, Pedestrianized segment of Española Way

WASHINGTON

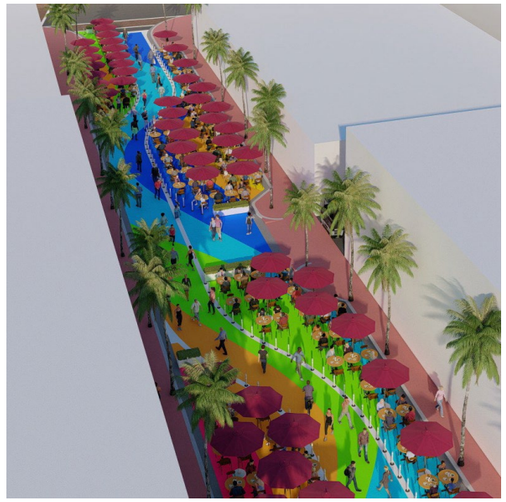

Washington to Collins

Tactical Urbanism project with painted asphalt and creation of usable social space within the re- purposed travel lanes.

COLLINS AVE



Collins to Ocean Dr

Tactical Urbanism project with painted asphalt

OCEAN

On-going Tasks

- On-going coordination with Miami-Dade County for approval of traffic study
- Pavement marking and striping plans for the tactical urbanism components to be completed by end of February 2023



Española Way | Tactical Urbanism

Next Steps

- **February:** Submit final draft design plans to City for internal review/approval
- **March - May:** County design review process and obtain County permit approval
- **April**: Host community meeting on Tactical Urbanism components
- **May**: Presentation to City Commission
- **June - July:** Procure JOC contractor and commence construction (construction schedule TBD)

Española Way | Tactical Urbanism
